

## *Final Agenda*

### **TBPOC CONFERENCE CALL August 29, 2013, 4:00pm – 5:00pm**

	<b>Topic</b>	<b>Presenter</b>	<b>Time</b>	<b>Desired Outcome</b>
<b>1.</b>	<b>CHAIR'S REPORT</b>	S. Heminger, BATA		Information
<b>2.</b>	<b>SAN FRANCISCO-OAKLAND BAY BRIDGE UPDATES</b>			
	a. SSO Update			
	1) Bridge Closure	T. Anziano, CT	5 min	Information
	2) LDW Construction Schedule*	D. Vilcheck, CT	5 min	Information
	3) PIO Update	A. Gordon, BATA	10 min	Information
	4) Opening Ceremony*	R. Rentschler, BATA	20 min	Information
	b. Bike Path Opening*	A. Fremier, BATA	10 min	Information
	c. Testing Update	T. Anziano, CT	10 min	Information
<b>3.</b>	<b>OTHER BUSINESS</b>			
<b>Upcoming TBPOC Conference Calls:</b> <b>Fri, August 30, 2013, 4:00pm – 5:00pm</b> <b>Sat, August 31, 2013, 4:00pm – 5:00pm</b> <b>Sun, September 1, 2013, 4:00pm – 5:00pm</b> <b>Mon, September 2, 2013, 4:00pm – 5:00pm</b> <b>Thurs, September 5, 2013: 1:00pm – 4:00pm</b>				

\* Attachments

\*\*Attachments in back of binder

\*\*\*Attachments to be sent under separate cover


***Weather Forecast***  
***Labor Day Weekend***

	<b>Wed, 8/28/2013</b>	<b>Thu, 8/29/2013</b>	<b>Fri, 8/30/2013</b>	<b>Sat, 8/31/2013</b>	<b>Sun, 9/01/2013</b>	<b>Mon, 9/02/2013</b>
<b>Oakland</b>						
High	79°F	80°F	83°F	77°F	76°F	77°F
Low	63°F	61°F	60°F	59°F	61°F	59°F
Humidity - Day	70%	70%	67%	72%	70%	73%
Humidity - Night	87%	86%	83%	76%	73%	79%
Day	Sunny	Mostly cloudy	Sunny	Mostly sunny	AM clouds PM sun	AM clouds PM sun
Night	Mostly cloudy	Mostly clear	Mostly clear	Partly cloudy	Partly cloudy	Partly cloudy
<b>Treasure Island</b>						
High	69°F	69°F	72°F	67°F	66°F	67°F
Low	59°F	60°F	60°F	58°F	59°F	58°F
Humidity - Day	85%	85%	80%	86%	82%	86%
Humidity - Night	97%	94%	91%	88%	84%	91%

Source: *weather.com*, 29Aug13

## Summary Schedule

# Draft

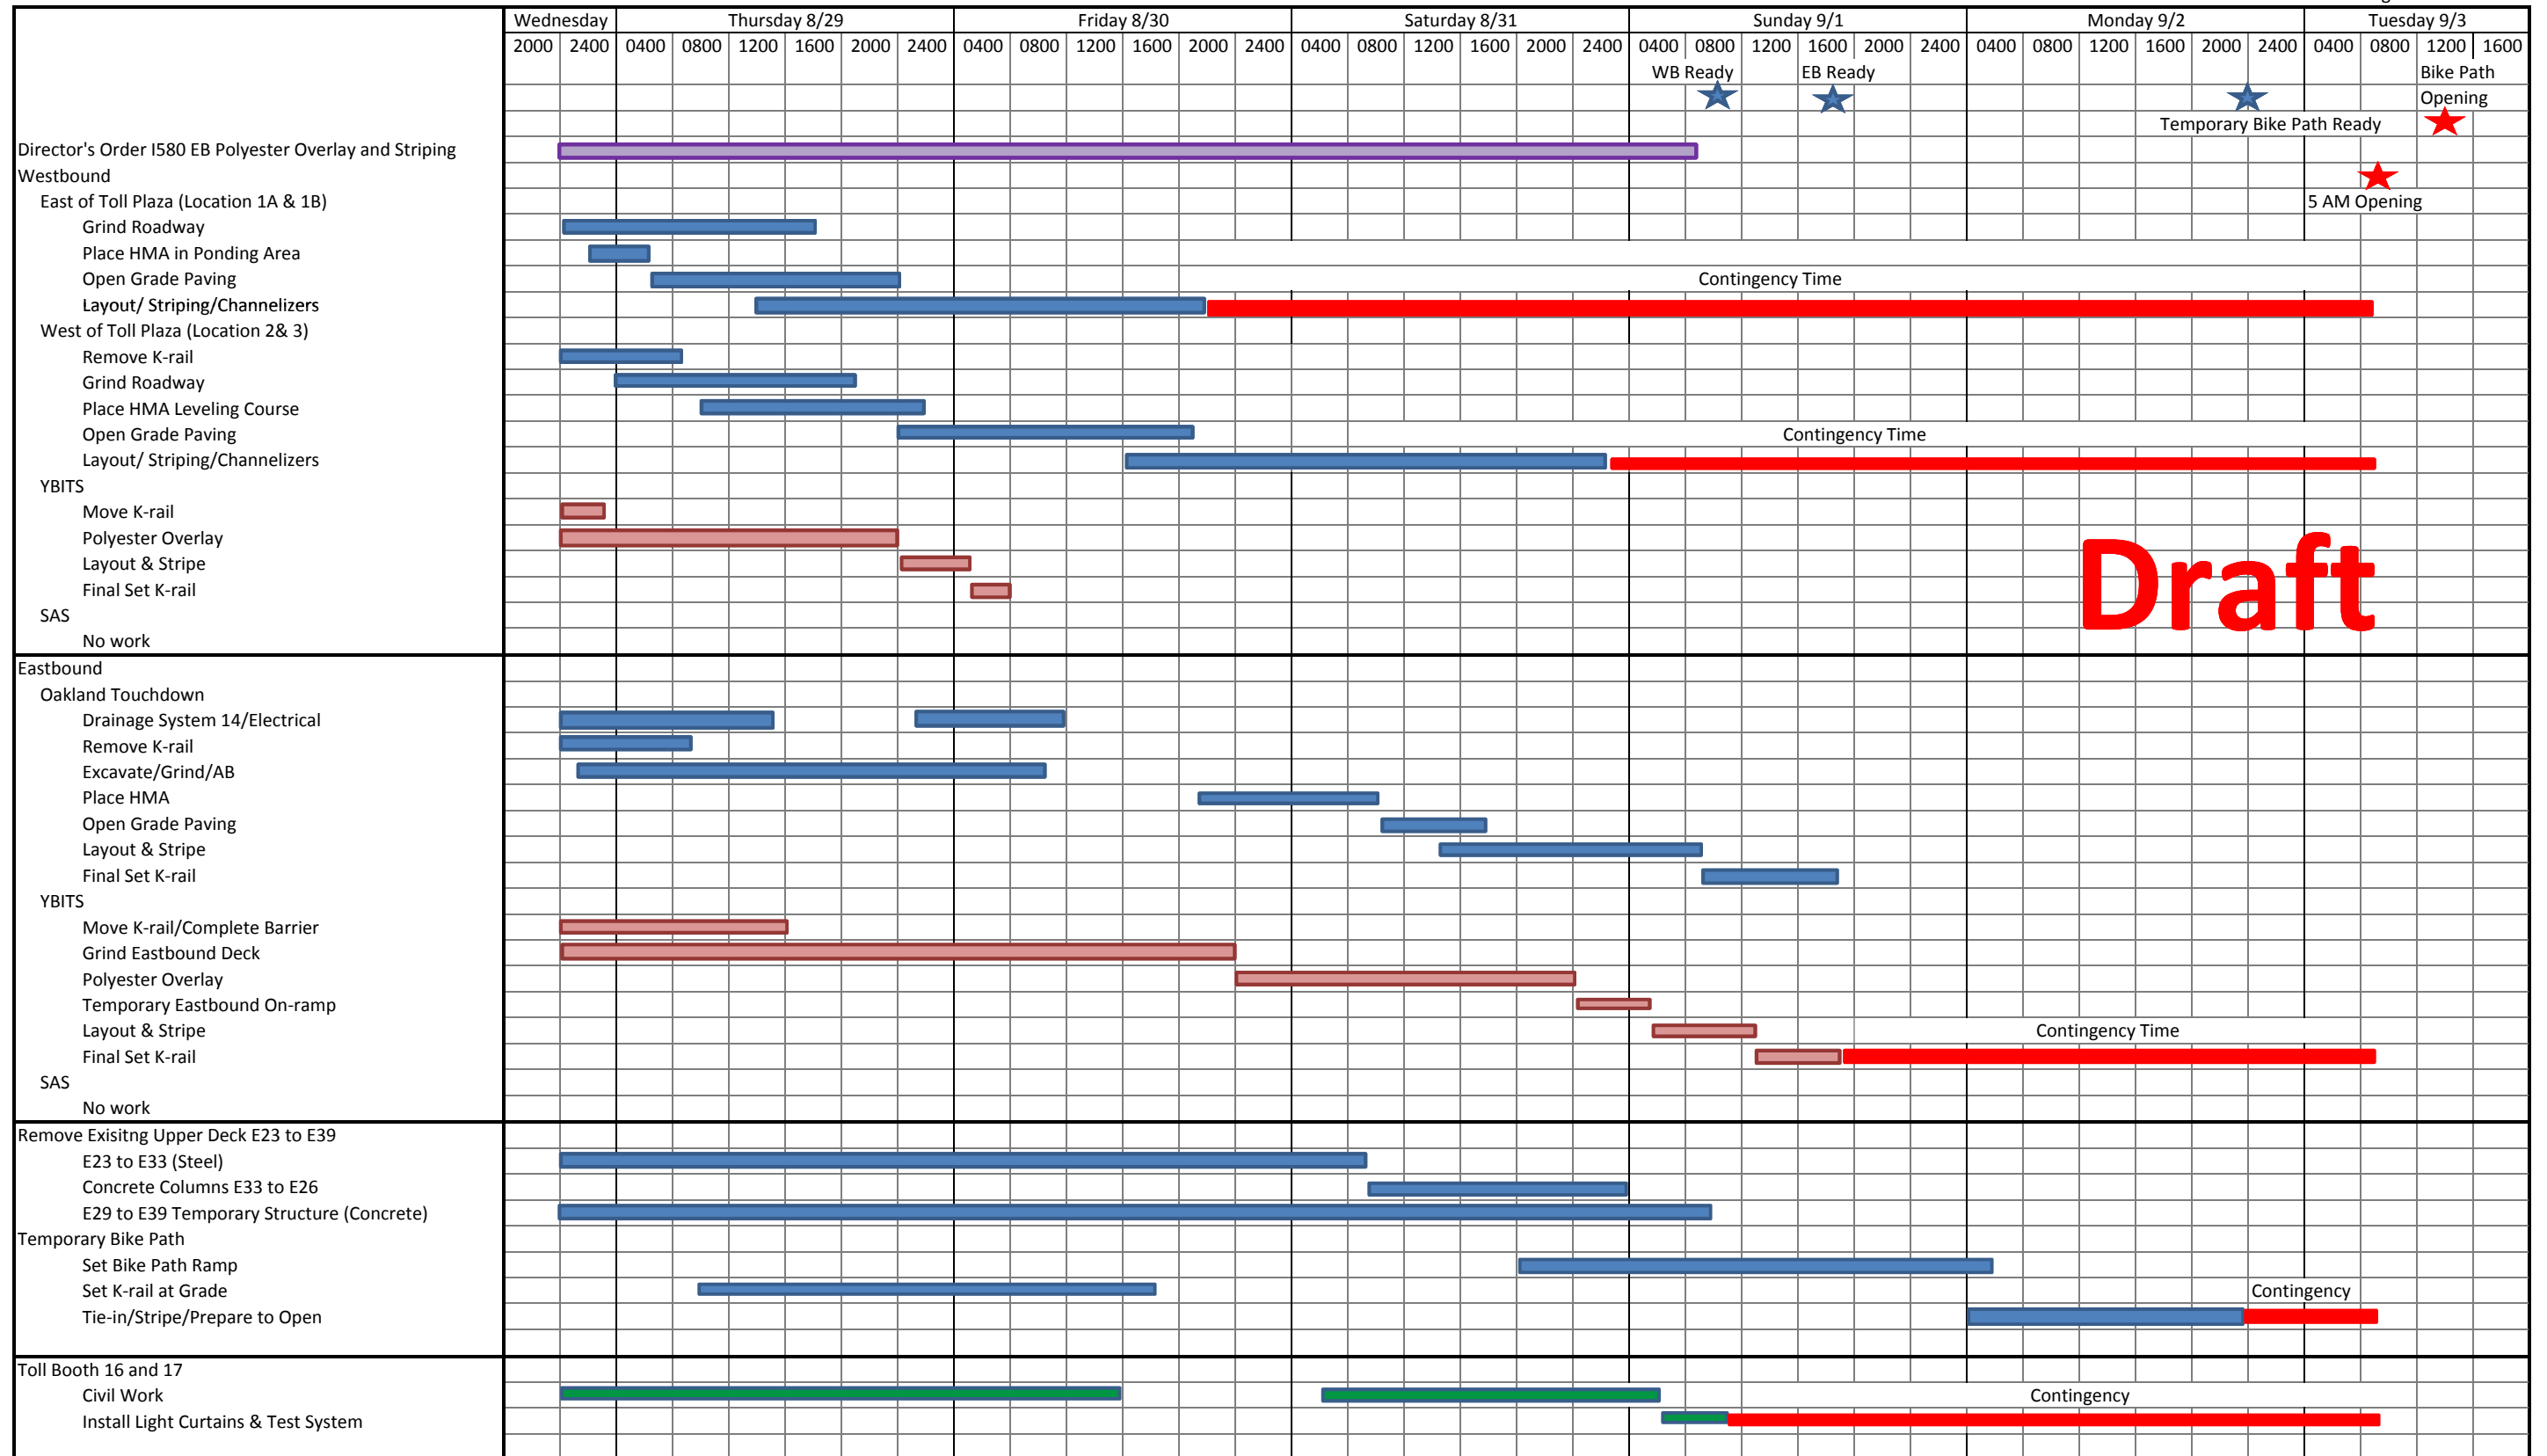



GRIND, PAVE, STRIPE

WEEKEND WORK

DRAFT

TOLL PLAZA

PERMANENT BARRIER BEFORE WEEKEND

FWI - WB GRIND & REPLACEMENT TO METERING LIGHTS BY CCO FUNDED BY TOLL BRIDGE REHAB ON OTD2 CONTRACT

- COLD PLANE
- PLACE 30mm HMA (OG) SURFACE
- PAVEMENT DELINEATION

K-RAILS INSTALLED DURING THE WEEKEND

K-RAILS INSTALLED PRIOR TO THE WEEKEND

(MCM)  
★ REMOVE PORTION OF STRUCTURE

OLD BRIDGE DEMOLITION (LEAD)

PERMANENT BARRIER BEFORE WEEKEND

1A

1B

2

3

EB

WB

EB

BIKE PATH SEGMENT 3

MAINTENANCE ROAD

BURMA RD.

YBJ-2 ACCESS

BURMA RD.

- ★ CONSTRUCT REMAINING PORTION OF EB-80 ROADWAY AND DRAINAGE SYSTEM
- ★ COLD PLANE EB-80 E LINE
- ★ PLACE 30 mm HMA (OG) SURFACE
- ★ PLACE TEMP RAILING (TYPE K) W/ SCREEN
- ★ PLACE TEMP/PERMANENT PAVEMENT DELINEATION

- ★ ERECT TEMP. BIKE PATH RAMP (MCM)
- ★ PLACE K-RAILS AT GRADE (FWI)
- ★ INSTALL DELINEATION

★ TEMP. BIKE PATH CROSSOVER PRIOR TO WEEKEND (MCM)

MAINT. RD. COMPLETED (S1-P2)

EB COMPLETED (STAGE 1)

TEMP. BIKE PATH RAMP


TEMP. BIKE PATH



**K-RAIL (INSTALL MONDAY NIGHT)**



**EASTBOUND ROUTE 80  
(LOWER DECK)**

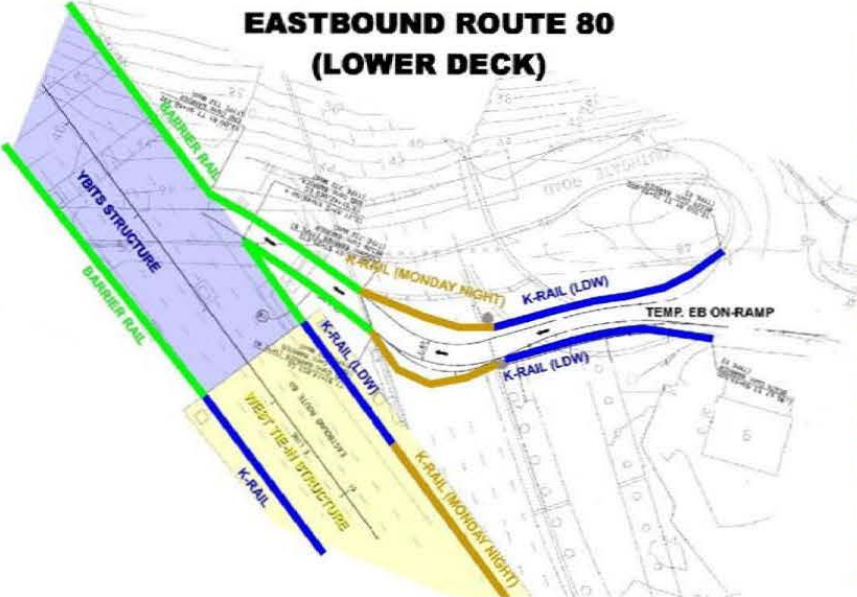



SFOBB CLOSURE = Wed 8/28 @ 8p - Tue 9/3 @ 5a

SFOBB (WEST SPAN)

Maintenance Work Chart							
Close Bridge @ 8p				Reopen Bridge Tue @ 5a (or prior)			
	Day (D) / Night (N) -->>	Wed 8/28 (N)	Thu 8/29 (D/N)	Fri 8/30 (D/N)	Sat 8/31 (D/N)	Sun 9/1 (D/N)	Mon 9/2 (D)
	Open Traffic Lane -->>	Lane 3	Lane 3 (both decks)	Lane 3 (both decks)	EB Lane 4, WB Lane 2 (South)	Lane 3 (both decks)	Lane 3
TOLL BRIDGE MTCE	James Province @ 510/435-9989 Greg Soria @ 510/459-9052 Joe Campos @ 510/715-9570		6a - 6p 1. Repair/Replace broken finger joints (Red) 2. Clean drain pan W-2 (Yellow) 3. Repair spalls adj to U.D. joint @W-1 (Green)	6a - 6p (continued) Add'l work: 1. Clean dirt @ W7 rocker post 2. Place missing screws into damper nuts 3. Grease pins @ tower rocker, cable links and within rocker post 4. Clenr Upper Deck drains 5. Remove dirt from under finger joints	6a - 6p Lane shifts to allow for finger joint work in Lane 3 (both decks)		
	Location-->>		Both decks (80% Upper) (W1 to W7)	Both decks (W1 to W7)	Both decks (W1 to W7)		
ELECTRICAL MTCE	Rene Fortaleza @ 510/715-8926 Kevin Lam @ 510/715-8110		All hours Lighting (on cables)	(continued )	(continued )		
	Location-->>		Both decks (W1 to W7)	Both decks (W1 to W7)	Both decks (W1 to W7)		
CA SEISMIC	Carl Petersen @ 916/322-9302 (Ca Strong Motion Instrumentation Program)		8a - 330p 1. Access seismic recorders @ W4 2. Recorder in a traffic enclosure at the East Anchorage (Yerba Buena Island), South side of the lower deck. 3. Sensors at the mid-point between W1 and W2 on both the South and North sides of lower deck.				
	Location-->>		Lower (W4)				
WEST BAY PAINT	Dave Annis @ 510/715-8646 Carlos Herrera @ 510/715-6733 Nina Kiniery @ 510/715-7323	Mobilize manlift from TI to WB Lane #1 Safway will stage from SF	Paint crew is 6a - 430p; Safway is all hours 1. W1 to W3 - WB suspender ropes (South side) 2. W4 - Clean and paint (both sides), paint sign structure 3. EB TI Off - Clean/paint wall	Paint crew is 6a - 430p; Safway is all hours (continued) Also, 1. EB scaffolding moving East. Contractor is Safway. Wed PM to Sat 8p(day/night) 2. Hanging a basket at W6, then W2 (Upper Deck)	(continued )		
	Location-->>	Upper (W1-W3)	Both decks (W1 to W7)	Both decks (W1 to W7)	Both decks (W1 to W7)		
SPECIALTY REGIONS	Pete Cortopassi @ 415/699-9055 Julian Gonzales @ 510/715-9128		6a - 6p 1. Refresh road striping and RPM's on all closed ramps 2. Replace/clean all signs	(continued )	(continued )		
	Location-->>		Both decks (W1 to W7)	Both decks (W1 to W7)	Both decks (W1 to W7)		
STRUCTURES MTCE	Bill Zanetich @ 510/910-5224 Mark Woods @ 510/385-6897	Mobilize from W. Bay paint in SF	7a - 8p See attached	7a - 8p See attached	7a - 8p See attached	8a - 1p See attached	
	Location-->>		Both decks (W1 to Tunnel)	Both decks (W1 to Tunnel)	Both decks (W1 to Tunnel)		
BAY LIGHTS	Saeed Shahmirzai @ 650/450-3507		All hours 1. Lighting maintenance 2. Baskets (4) in day, manlifts (4) at night. WILL LEAVE OVERNIGHT IN LANE 2 or 4	(continued )	(continued )	(continued )	
	Location-->>		Upper deck (W1 to W7)	Upper deck (W1 to W7)	Upper deck (W1 to W7)		
TUNNEL LIGHTING	Saeed Shahmirzai @ 650/450-3507	Midnight from TI	7a - 7p 1. Install lights on Upper Deck 2. Remove conduit on Lower Deck	(continued )	(continued )	(continued )	
	Location-->>		Both decks (Tunnel)	Both decks (Tunnel)	Both decks (Tunnel)		
CT SURVEY	CJ Vandegrift @ 707/321-7488		0600 - 1600 1. Setting sticks on targets (18" x 18" - on curb) 2. Mobile scanning	(continued )	(continued )		Noon-3p 3 roundtrip survey scans
	Location-->>		Both decks (W1 to W7)	Both decks (W1 to W7)	Both decks (W1 to W7)		

SFOBB CLOSURE = Wed 8/28 @ 8p - Tue 9/3 @ 5a

Maintenance Work Chart

EAST OF SFOBB

Close Bridge @ 8p				Reopen Bridge Tue @ 5a (or prior)			
	Day (D) / Night (N) ->>	Wed 8/28 (N)	Thu 8/29 (D/N)	Fri 8/30 (D/N)	Sat 8/31 (D/N)	Sun 9/1 (D/N)	Mon 9/2 (D)
	Open Traffic Lane ->>	None	None	None	None	None	None
EAST BAY MTCE	Amy Fain @ 510/715-8199 Sherrie Swaim @ 510/715-8043 Ismael Vega @ 510/715-6204		6a - 430p 1. Vegetation control and litter abetement (Powell St to Toll Plaza) 2. Attenuator replacement @ NB880 HOV connector (left) 3. Graffiti 4. Clean drains 5. Repair fence on WB80 (Powell St to Horseshoe) 6. Crack sealing (on WB580, 24 to Maze) 7. Median at WB580 8. Delineation, as needed.	(continued )	(continued )		
	Location-->>		WB80, NB880, WB580	continued	continued		
ELECTRICAL MTCE	Rene Fortaleza @ 510/715-8926 Kevin Lam @ 510/715-8110		All hours Replace light fixtures with LEDs	(continued )	(continued )	(continued )	
	Location-->>		580E, 580W, 80/580 IC	continued	continued		
CT CONSTRUCTION	Chris Havel @ 510/385-8155		All hours. 80/580 striping, joints (EB only)	(continued )	(continued )	(continued )	
	Location-->>		EB80/580 connector	continued	continued		
STRUCTURES MTCE	Bill Zanetich @ 510/910-5224					8a - 1p See attached	
	Location-->>		Maritime Offramp (Horseshoe bridge)	continued	continued	continued	
SPECIALTY REGIONS	Pete Cortopassi @ 415/699-9055 Tim Lowe @ 510/715-6176		6a - 6p 1. Refresh road striping and RPM's on all closed ramps 2. Replace/clean all signs	(continued )	(support only)		
	Location-->>		Maritime Offramp (Horseshoe bridge)	continued	continued	continued	
WEST BAY PAINT	Dave Annis @ 510/715-8646 Carlos Herrera @ 510/715-6733 Nina Kiniery @ 510/715-7323		Paint two EB sign structures at Toll Plaza				
	Location-->>					Eb Toll Plaza	
METROPOLITAN TRANSPORTATION COMMISSION	Jeff Gerbracht @	See attached	See attached	See attached	See attached	See attached	See attached
	Location-->>	Toll Plaza	Toll Plaza	Toll Plaza	Toll Plaza	Toll Plaza	Toll Plaza
CT CONSTRUCTION	Lawrence Loi @ 510/867-6035	See attached	Day hours Add EB barrier	(continued )	(continued )	(continued )	(continued )
CT CONSTRUCTION	Frank Gorham @ 510/385-6758 Jim Hanson @ 510/385-6756 Jennifer Egawa @ 510/867-6176		(daytime) Median landscaping	(continued )			
	Location-->>		Toll Plaza	Toll Plaza	Toll Plaza		

WEST OF SFOBB

Reopen Bridge Tue @ 5a (or prior)

Close Bridge @ 8p		WB80 detour: 4th St Offramp				WB80 detour: 7th St Offramp	
	Day (D) / Night (N) ->>	Wed 8/28 (N)	Thu 8/29 (D/N)	Fri 8/30 (D/N)	Sat 8/31 (D/N)	Sun 9/1 (D/N)	Mon 9/2 (D)
	Open Traffic Lane ->>	None	None	None	None	None	None
WEST BAY MTCE	Chris Balingit @ 650/333-5168 Francisco Chavez @650/444-7238		6a - 6p (?) 1. 4th and 7th St landscape maintenance 2. Drain clean/sweeping (2 vacuums) Notes: no WB 4th/7th Onramp closures required.	(continued )	(continued )	(continued )	
	Location-->>		EB and WB (7th St to SFOBB)	(continued)	(continued)		
ELECTRICAL MTCE	Rene Fortaleza @ 510/715-8926 Kevin Lam @ 510/715-8110		All hours Replace light fixtures with LEDs	(continued )	(continued )	(continued )	(continued )
	Location-->>		EB and WB (5th St to SFOBB)	(continued)	(continued)		
SPECIALTY REGIONS	Pete Cortopassi @ 415/699-9055 Julian Gonzales @ 510/715-9128		6a - 6p 1. Refresh road striping and RPM's on all closed ramps 2. Replace/clean all signs	6a - 6p (continued )	6a-Noon (continued )		
	Location-->>		EB and WB (7th St to SFOBB)	(continued)	(continued)		



#	Task	Location	Action Items	Contractor	Due Date
1	Need PCMS' picked up from BART Strike	Adjacent to fence	Picked up on 8/19/13.	Aegis	Done
2	Swinerton Hard Hat	Karin Betts	Zach to deliver to toll plaza.	Swinerton	Done
3	ATCAS II Tunnel Equipment Relocation	Pedestrian/Utility Tunnels	Lanes 18-20 cutover on the nights of 8/20 and 8/21.	Aegis	Done
4	South Side Tunnel Cleanup – Part I (8/21 at 10pm)	Between IERBY's and Toll Operations	1. Sweep stairs and floor 2. Power wash walls (remove cobwebs) 3. Remove standing water	Universal	Done
5	South Side Tunnel Cleanup – Part II (8/22 at 8am)	Between IERBY's and Toll Operations	1. Replace 60w light bulbs with 100w light bulbs 2. Paint walkway railings	Aegis	Done
6A	Install French Drain, grade area to ensure drainage	Adjacent to new barrier	Drain completed on 8/22	Platinum	Done
6B	Sprinklers/Landscaping repair near walkway	Adjacent to barrier	Landscaping can't complete until after barrier is done.	Platinum	8/26/13 5:00 PM
7	CMS Cabinet Tunnel Equipment Relocation	Pedestrian/Utility Tunnels	Ver-mac suggests not splicing wires. Need to re-run fiber.	Aegis	8/27/13 5:00 PM
8	Trim plants at Operations Building	Walkway to Building	Landscape technician (Rigo) to complete work	RMT	8/28/13 12:00 PM
9	Windows and Roof Repairs at IERBY's Paint Shop	IERBY's Paint Shop	Rhett has contact information to find out current status.	Aegis	8/28/13 5:00 PM
10	Booth 17 Equipment Removal prior to demolition (Clock, intercom, indicator light box, phone, signs)	Booth 17	Start at 8:00pm, must complete in 1.5 hours. Fix 1.10 and 1.18 because they are there at night?	Aegis	8/28/13 9:30 PM
11	Send statistics to PIO (John/Randy)	N/A	First deliverable on 8/29 at 12:00pm.	BATA	8/29/13 12:00 PM
12	Wash toll booths in preparation for painting	Booths 1-16	Start at 8:00am using squeegee on areas that may be painted.	Aegis	8/29/13 12:00 PM
13	Complete Safety Walkthrough Punchlist Items	East Parking Lot	Paint arrow (8/29), sign, two other things.	Platinum	8/29/13 5:00 PM
14	Plaza PM's and CMS Repairs of BATA equipment	Toll Plaza	Finish early to check if 3, 7, 10(cms/light), 18 are fixed.	Aegis	8/29/13 5:00 PM
15	Install two 25 mph speed limit signs	Lanes 2 and 7	Purchase new signs that have the correct font.	Aegis	8/29/13 5:00 PM
16	Remove unneeded FasTrak railings	Toll Plaza	3 in lane 5, 1 in lane 9. Fill holes with sand/concrete.	Aegis	8/29/13 5:00 PM
17	SWPPP Inspection Repairs - Rock install (Started 8/22)	Area adjacent to Booth #1	Final install shall not be in conflict with paving.	Platinum	8/29/13 5:00 PM
18	Replace broken toll signs	Toll Plaza	Lanes 1 (2), 10, 12, reuse toll signs from lane 17.	Aegis	8/30/13 5:00 PM
19	Replace gate arms (Two day project - start on 8/29)	Toll Plaza	Change from orange to red, maximize number of red stripes.	Aegis	8/30/13 5:00 PM
20	Paint flashing light base green	Toll Plaza	Aegis has 7 cans, may need to purchase more.	Aegis	8/30/13 5:00 PM
21	Remove three malfunctioning drinking fountains	Toll Plaza	Rhett knows how to cap, need to paint behind them.	Aegis	8/30/13 5:00 PM
22	Touch up booth and wall paint	Most Toll Lanes	Need booths to be dry prior to starting.	Aegis	8/30/13 5:00 PM
23	Power wash Toll Operations Building	South Side	Start at 10pm on 8/30. Include the pump house.	Universal	8/31/13 5:00 AM
24	Paint new gantry unistrut (Bag existing equipment)	Lanes 18-20	<b>Confirm if 4 gallons given to Aegis by Proven will adhere to the HG surface finishing.</b>	Aegis	8/31/13 5:00 PM
25	SFOBB Lane 17 ORT Conversion	Toll Plaza	Work will also occur in lane 16 over the weekend.	Flatiron	8/31/13 5:00 PM
26	Power wash Toll Operations Building	North Side	Includes glass on walkway. Start at 10pm on 8/31.	Universal	9/1/13 5:00 AM
27	Hang CMS above lane 17	Toll Plaza	<b>Caltrans reviewing mounting details, draft given to Aegis.</b>	Aegis/Crane	9/1/13 12:00 PM
28	Remove CMS on existing Bay Bridge (Deanna to decide)	Old Bay Bridge	<b>Schedule the same day as Lane 17 CMS install.</b>	Aegis/Crane	9/1/13 5:00 PM
29	Replace HPS canopy lighting with LED's	Toll Plaza (51 lights)	Proof of concept completed on 8/23. Fixtures being built.	Aegis	9/1/13 5:00 PM
30	Tunnel Equipment Removal	Pedestrian Tunnel	Remove once ORT Equipment has been abandoned.	Aegis	9/1/13 5:00 PM
31A	Sticker Removal	Toll Plaza	Start at 3:00pm. All three happen concurrently.	Universal	9/1/13 7:00 PM
31B	Weed control around toll plaza	Toll Plaza			
31C	Remove trash within crash cushions, around building	Lanes 1-15			
32	Power wash Toll Plaza (Start: 9/1 at 10pm)	Lanes 1-15, 16 if available	Top of the toll booth down. Clean standing water in booths.	Universal	9/2/13 5:00 AM
33	Clean the inside of the toll booths	Toll Plaza	Captain Dhillon will have his staff perform the work.	Caltrans	9/2/13 12:00 PM
34	Chain Cutting Ceremony in front of toll plaza	Toll Plaza	All work must be completed by this time.	N/A	9/2/13 5:00 PM

Comments that may turn into action items:

A.	Full load test of generator/ups system?
B.	Photos for Raymond
C.	Clean YBI tunnels? CT is trying, but can't during closure.
D.	CT is taking out the Cohu cameras?
E.	Paint pole that's in storage? Ask Kerry.
F.	Clean the underside of the canopy?

\* Items in **bold** have open questions.

JEFF GERBACHT/MTC

#	INSPECTION ACTIVITY	LOCATION	Wed, Aug 28	Thurs, Aug 29	Fri, Aug 30	Sat, Aug 31	Sun, Sept 1	Mon, Sept 2	Tues, Sept 3
			20 21 22 23 0 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 0	1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 0	1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 0	1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 0	1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 0	1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 0	1 2 3 4 0
1	Upper & Lower Deck Surfaces, Expansion Joints + Upper Deck Floor System (w/ bucket truck)	YBI TUNNEL + E & W PORTALS		<div></div>					
2	Upper Deck Floor System (w/ 2 manlifts)	WEST SPAN - Lower Deck (SF - YBI)		<div></div>	<div></div>	<div></div>			
3	Upper & Lower Deck Surfaces, Expansion Joints, Railing, Trusses	WEST SPAN - Both Decks (SF - YBI)		<div></div>	<div></div>	<div></div>			
4	Continuous Span Bearings	WEST SPAN - Lower Deck (SF Anch & W1)		<div></div>					
5	Seismic Dampers	WEST SPAN - Lower Deck (SF Anch)		<div></div>					
6	Suspender Ropes - Vibration Frequency Measurements (w/ bucket truck)	WEST SPAN - Upper Deck (SF - YBI)		<div></div>	<div></div>	<div></div>			
7	Steel Bridge Inspection - underside from EB & WB 80 (w/ Uunder Bridge Inspection Truck)	Maritime Offramp (Horseshoe bridge)					<div></div>		

Contact person - Bill Zanetich - (510) 910-5224





Bay Bridge East Span Grand Opening  
Monday, September 2, 2013

3:00 - 6:30 p.m  
Location: Bridge Yard



Run of Show v11

1	2:00 PM	1:00:00	3:00 PM	Doors and Walk-in	<ul style="list-style-type: none"> <li>Exhibit Displays: MOS video</li> <li>Main screens video loop - MOS collection of images/video of old and new bridge</li> </ul>
		15 min			<ul style="list-style-type: none"> <li>Exhibit Displays: MOS video</li> <li>Main screens video loop - Sound from Video</li> </ul>
2	3:00 PM	0:02:00	3:02 PM	Workers and dignitaries take stage	
3	3:02 PM	0:02:00	3:04 PM	Start of the Show	<ul style="list-style-type: none"> <li>Choir goes to Position - In front of stage</li> <li>VOG for Color Guard</li> </ul>
4	3:04 PM	0:00:15	3:04 PM		VOG: "Ladies and Gentlemen, please rise for the presentation of colors by the Oakland Military School honor guard."
5	3:04 PM	0:00:45	3:05 PM	Presentation of Colors by Oakland Military School	
6	3:05 PM	0:00:15	3:05 PM		<ul style="list-style-type: none"> <li>VOG: "And, now, singing our National Anthem. The Pacific Boychoir Academy."</li> <li>Color Guards move Stage Right, allowing clear view to choir</li> </ul>
7	3:05 PM	0:02:00	3:07 PM	National Anthem by Pacific Boychoir Academy	Following Anthem, Color Guard and Choir Exit
8	3:07 PM	0:00:15	3:07 PM	VOG intro - Steve Heminger	VOG: "Ladies and Gentlemen, Executive Director, Metropolitan Transportation Commission...and our master of ceremonies...Steve Heminger."
9	3:07 PM	0:05:00	3:12 PM	Steve Heminger - Welcome	<ul style="list-style-type: none"> <li>Thank Color Guard and Choir</li> <li>Begin to recognize notables: Electeds, CTC/MTC Commissioners, other luminaries (a process that will continue at several breaks in program)</li> <li>Introduce Rev. Dr. J. Allen</li> </ul>
10	3:12 PM	0:01:00	3:13 PM	Invocation - Rev. Dr. J. Allen Smith Jr.- Allen Temple Baptist Church	Will be seated on stage and provide a short opening Prayer.
11	3:13 PM	0:00:15	3:13 PM	Steve intro - Juan Felipe Herrera	Poetry Reading – Ca State Poet Laureate
12	3:13 PM	0:03:00	3:16 PM	Juan Felipe Herrera	Show poem on screen as it is recited
13	3:16 PM	0:03:00	3:19 PM	Steve Heminger - New and Old Bridge Segment • Opening Observations	Slide support – images and graphics (produced by Joe Curley)
14	3:19 PM	0:00:15	3:20 PM	Steve Heminger - intro Mayor Quan	Oakland Mayor Jean Quan
15	3:20 PM	0:04:00	3:24 PM	Mayor Quan	



Bay Bridge East Span Grand Opening  
Monday, September 2, 2013

3:00 - 6:30 p.m  
Location: Bridge Yard



Run of Show v11

16	3:24 PM	0:00:15	3:24 PM	Mayor Quan intro - Barbara Lee	• Congresswoman Barbara Lee
17	3:24 PM	0:04:00	3:28 PM	<b>Barbara Lee</b>	
18	3:28 PM	0:00:15	3:28 PM	Barbara Lee - intro Darrell Steinberg	• State Senate President pro Tempore, Darrell Steinberg
19	3:28 PM	0:04:00	3:32 PM	<b>Darrell Steinberg</b>	
20	3:32 PM	0:00:15	3:32 PM	Darrell Steinberg - intro Loni Hancock	• State Senator Loni Hancock
21	3:32 PM	0:04:00	3:36 PM	<b>Loni Hancock</b>	• Ask Assembly Members Skinner and Bonta to rise for recognition (onstage but not speaking)
22	3:36 PM	0:00:15	3:37 PM	Loni Hancock - intro Mark Leno	• State Senator Mark Leno
23	3:37 PM	0:04:00	3:41 PM	<b>Mark Leno</b>	
24	3:41 PM	0:00:15	3:41 PM	Mark Leno - intro Robbie Hunter	• President, State Building Construction Trades Council, Robbie Hunter
25	3:41 PM	0:04:00	3:45 PM	<b>Robbie Hunter</b>	
26	3:45 PM	0:00:15	3:45 PM	Robbie Hunter - intro Mike Flowers	• Mike Flowers, CEO, American Bridge Co.
27	3:45 PM	0:04:00	3:49 PM	<b>Mike Flowers</b>	• Shout out to other contractors: Fluor Corp., MCM Construction, Kiewit/FCI/Manson, Flatiron West, C.C. Myers, West Bay Builders
28	3:49 PM	0:03:00	3:52 PM	<b>Steve Heminger - In Memoriam</b>	• Music Plays under Steve's comments • Woman who died – recognize family if in audience • Photos support segment • EDAP (4-5 representatives) • TBPOC – Bimla Rhinehart
29	3:52 PM	0:00:15	3:52 PM	Steve intro - Mayor Lee	• San Francisco Mayor Ed Lee
30	3:52 PM	0:04:00	3:56 PM	<b>Mayor Lee</b>	
31	3:56 PM	0:00:15	3:57 PM	Mayor Lee intro - Amy Rein Worth	• BATA Commissioner, Amy Rein Worth
32	3:57 PM	0:03:00	4:00 PM	<b>Amy Rein Worth</b>	• Standby for Women of the Bridge video
33	4:00 PM	0:01:00	4:01 PM	• Women of the Bridge Video • Brief Remarks	





Bay Bridge East Span Grand Opening  
Monday, September 2, 2013

3:00 - 6:30 p.m  
Location: Bridge Yard



Run of Show v11

34	4:01 PM	0:00:15	4:01 PM	Amy Rein Worth intro - James Ghielmetti	• CTC Chair James Ghielmetti
35	4:01 PM	0:04:00	4:05 PM	<b>James Ghielmetti</b>	
36	4:05 PM	0:02:00	4:07 PM	<b>Steve Heminger - "Life of..." Segment</b>	<ul style="list-style-type: none"> <li>• Music Plays under Steve's comments</li> <li>• Split screen slides with now and before images</li> <li>• 4 different Brian's (<b>Brian Peterson ABF</b>, <b>Brian Mayhew TBPOC</b>, <b>Brian Maroney CalTrans</b>, <b>Brian Kelly Legislative</b>)</li> </ul>
37	4:07 PM	0:00:15	4:07 PM	Steve Heminger - intro Brian Kelly	• California State Transportation Agency Secretary Brian Kelly
38	4:07 PM	0:04:00	4:11 PM	<b>Brian Kelly</b>	
39	4:11 PM	0:00:15	4:11 PM	Brian Kelly intro - Malcolm Dougherty	• Caltrans Director Malcolm Dougherty
40	4:11 PM	0:04:00	4:15 PM	<b>Malcolm Dougherty</b>	
41	4:15 PM	0:00:15	4:16 PM	Malcolm Dougherty - intro Lt. Gov Gavin Newsom	• Lt. Gov. Gavin Newsom
42	4:16 PM	0:10:00	4:26 PM	<b>Lt. Gov Gavin Newsom - Keynote Speaker</b>	
43	4:26 PM	0:01:00	4:27 PM	Troll Video Roll	<ul style="list-style-type: none"> <li>• Provided by Mark Jones</li> <li>• Workers bring Troll to stage (covered) during video roll</li> </ul>
44	4:27 PM	0:03:00	4:30 PM	Steve Heminger - Troll Segment	<ul style="list-style-type: none"> <li>• Steve will have very specific instructions for those who are walking to watch the chain cutting and for those who are driving</li> <li>• Photo op for those who stay at Bridge Yard</li> </ul>
45	4:30 PM	0:15:00	4:45 PM	Transition to Chain Cutting	<ul style="list-style-type: none"> <li>• Displays: MOS video</li> <li>• Main screen video loop - collection of images/video of old and new bridge</li> </ul>
46	4:45 PM	0:30:00	5:15 PM	Chain Cutting Broadcast	
47	5:15 PM	0:00:00	5:15 PM	End onstage production	<ul style="list-style-type: none"> <li>• Begin Reception</li> <li>• Continue main screen video loop</li> </ul>
48	5:15 PM	1:30:00	6:45 PM	Reception at Bridge Yard	

PRESENTATION THEATER

724 Seated  
20 ADA  
28 Presenter Chairs

GREEN ROOM

VIP

STAGE  
ENTRANCE

SEATED GUEST  
ENTRANCE

SEATED GUEST ACCESS SHOOT

EXIT

ADA

6ft. Wide Aisle

73'-8 1/2"

450 Reserved Seats  
20 ADA

6ft. Wide Aisle

56 Reserved  
Seats

194 Seats

VIDEO 1

VIDEO 2

AUGUST 29, 2013 1:00 PM

EXIT

100 West Ohio Avenue  
Richmond, CA 94804  
(510)232-5030; FAX (510)232-1350  
E-mail: scotw@hartmannstudios.com

The concepts, designs, plans and graphics transmitted herewith are only for evaluation by the intended recipient of a proposal made by Hartmann/Impact, and cannot be otherwise used or made available to third parties without our prior written consent.  
2013 ALL RIGHTS RESERVED ©



New East Span Opening Overview  
Bridge Yard



Print Date: Aug 29, 2013  
Show Date: Sept.2013  
Drawn By: Thomas M  
SHEET #  
**6.00**



## Event Schedule for Monday, September 2

### Oakland Span of the Bay Bridge Opening

**1:45 p.m.** – Arrival. Access parking from West Grand Avenue, go left on Burma Road. The parking lot is on your left at Burma Road and Maritime.

**2:00 - 2:45 p.m.** -- Come early to view exhibits on the design and construction of the New East Span at the event site, the newly restored Bridge Yard

**3 p.m.** -- Ceremony begins

**4 p.m.** -- Walk to Toll Plaza for Chain Cutting Ceremony

**6 p.m.** Bridge Yard event site closes.

#### Attire:

The weather is expected to be warm and sunny. We recommend that all guests wear comfortable, closed-toe walking shoes (no one will be admitted on the Toll Plaza for the Chain Cutting Ceremony without closed-toe shoes).

#### What else?

Light refreshments will be served.

## Event Schedule for Tuesday, September 3

### Oakland Span Bicycle and Pedestrian Bridge Opening

**9:00 a.m.** – Meet at the front of City Hall for the Mayor's bike ride to the new Bike Bridge

**10:00 a.m.** – If driving or walking to the media event, arrive at parking area, walk to media point near the new bike bridge

**10:30 a.m.** – Media event with the Mayor and other Special Guests only

**12:00 p.m.** – Bike and Pedestrian Bridge opens to general public

#### Attire:

The weather is expected to be warm and sunny. We recommend that all guests wear comfortable, closed-toe walking or riding shoes, as the terrain to the new bike and pedestrian bridge may still be rough.

### 1. **Oakland Span of the Bay Bridge Opening Details**

Iris Starr and Jim MacIlvaine are coordinating with Caltrans, MTC, and BATA. Follow-up meeting/conference call **completed** with those agencies on Wednesday 9/28.

- Opening: Monday September 2 at 3pm.
- 800-900 invitees, but no general public event will be held.
- By invitation only; Mayor, Council Members, and City Administrator will be invited by MTC/Caltrans
- Parking at Film center lot. Go over bridge to Army Base along West Grand, right on Burma. Lot is at corner of Burma and Maritime.
- AC Transit shuttle from WO BART for ceremony.

### 2. **Mayor's Separate Oakland Span of the Bay Bridge Bike Bridge Opening Details**

- **Field meeting now on Monday September 2 at 10am in the PIO office on Pier 7. Harry Hamilton to attend.**
- Opening: Tuesday September 3 at 10:30 am.
- At 9 am, Mayor Quan and staff (open to "all") will ride from City Hall, down 14<sup>th</sup> Street, up Mandela Parkway, over on Shellmound, and onto the Bay Trail connection that leads to the bridge. Escort will be provided by East Bay Bicycle Coalition. Caltrans maintenance to open roadway and trail east end gates by 10:00am. (Sean Maher – lead)
- Speakers/ attendees include: **Mayor Quan, Oakland City Administrator, Mayor of Emeryville/ City Administrator, MTC Chair Amy Worth, East Bay Bicycle Coalition/Dave Campell, Zuckerman family, WOBO.** Non-speaking guests: Steve Heminger, Malcolm Dougherty, Andre Boutros, **BCDC/Brad McCrea, ABAG/Bay Trail Laura Thompson.** (Sean Maher-Lead)
- AC Transit shuttle from WO BART available for ceremony. (Pledged by Any Fremier)
- A limited amount of parking will be available on Burma Road for drivers (media, disabled, emergency). (Port- Mike Obrien/City-John Monetta)
- **The Film Center Lot will be available** for drivers to park. The bike/ped bridge is about ¼ mile along the trail from the parking lot. (Kerry Roach/ John Monetta)
- Golf carts/small off-road vehicles for carrying media/disabled will be available to shuttle people from Film Lot to media site. (Caltrans District 4 Bob Haas)
- BATA/ Caltrans will provide podium, microphone, sound, etc. (Caltrans District 4 Bob Haas)
- MTC to print Burma Shave signs (Andy Fremier)
- **City to install Burma Shave signs (DIO ???)**
- City of Oakland to provide bike chain and scissors. (Jim MacIlvaine)
- City of Oakland to hang temporary signs on Caltrans screens and over "no parking" signs on Burma Road. (Peter Chun **DIO ?????**)
- City of Oakland to remove leaning light pole on Burma Rd –removal planned for 8/28. (Gus Amirzehni/DIO)
- **Bike Bridge open to the public at 12 noon**

### 3. Construction - Truck Traffic Routing

Wlad Wlassowsky, OPD Peter Lau, Peter Chun and Iris Starr have been coordinating on the routing of dump trucks (asphalt) from the Pleasanton Factory to the Bay Bridge. **Need a PWA Traffic representative in the command center in case trucks need to be re-routed.**

- Construction trucks will be traveling on I-580 through Oakland, having received an exemption from the truck prohibition through the long weekend. Initially Caltrans had planned to bring the trucks (at the peak, one truck per minute and about 2500 trucks altogether) in on Hwy-580 to Hwy 980 to West Grand Avenue (via the 27<sup>th</sup> Street exit) and on West Grand to the Bay Bridge. We agreed to accommodate this route, **if absolutely needed**, by modifying the traffic signals along this corridor. However, we pushed back hard on the use of West Grand Avenue because it cuts through West Oakland community that is hypersensitive to truck traffic and diesel emissions.
- Caltrans has since agreed that they will try not to use W. Grand Avenue to route trucks (starting Wed. night until the paving work is done hopefully on Saturday). They however need W. Grand as a contingency plan if the Hwy 580 access plan breaks down.
- If contingency plan used, Caltrans takes the blame. Verbal agreement between Steve Heminger and Iris that the route will be repaved to better than prior condition after use.
- **Steve Heminger/Ken Terpstra request meeting with Council Member McElhaney's Office ASAP. Wlad has already let Casey Farmer know verbally that we may be allowing this daytime operation on Grand Avenue. MTC/Caltrans ready to deliver flyers to West Oaklanders regarding the contingency plan. Do we need to vet this, or let it be their operation?**
- As of 8/28 1:35 pm, the verbal truck routing plan calls for the following routes from Pleasanton. **CHP will provide traffic control:**
  - A. Overnight, 8 pm to 5 am. – Hwy 580 west to Hwy 238 west to Hwy 880 north to 880 Frontage Road via the 7<sup>th</sup> Street Exit to West Grand to the Bay Bridge Structure.
  - B. Daytime, 5 am to 8 pm. – Hwy 580 west to Bay Bridge Structure. Includes using the truck restricted portion of Hwy 580 from Foothill Blvd (in San Leandro) to Grand Avenue. Caltrans gave themselves permission for this event.
  - C. Daytime Contingency, 8 am to 8 pm – Hwy 580 west to Hwy 980 west to 27<sup>th</sup> Street Exit to southbound Northgate Ave to West Grand west to the Bay Bridge. CHP may escort trucks on Hwy 580 from 5 am to 10 am to get through this critical time. Also if this contingency plan is used OPD will stage officers at the critical intersections which we have determined to be West Grand at Northgate and West Grand at San Pablo.
  - D. The expectation is there would be 20 – 24 Dump Trucks an Hour during the day.

### 4. Other items

- East Bay Bike Coalition event on Tues @ 6pm. **Leaving from West Oakland Bart, they still plan to ride over on 7<sup>th</sup> Street and up Maritime. I have advised them against this route.** They expect approximately 500 bicyclists. The bike/pedestrian path will close at 8:00pm on Tues, at sunset thereafter.
- Bike path to be closed for one month in 6-12 months out in order to remove the temporary trestle @ Oakland touchdown point and make the permanent connection to the Treasure Island.
- Caltrans has planned no other future access to the new bike bridge other than the trail from Emeryville, and at this point no parking will be available on any of the property nearby (Army Base transfers to Tagami on September 6, 2013).
